

Summary Overview

Filter

Year

2024

▼


Year Month

2024-Nov

▼

Overall Progress Status

Project Delayed



All Block

Block

All

Piling Progress

73.58%!  
Master Program Plan Progress:  
100.00%

PPVC Progress

Casting Progress

15.61%!  
Master Program Plan Progress:  
100.00%

Delivery Progress

5.14%!  
Master Program Plan Progress:  
99.67%

Fit Out Progress

1.54%!  
Master Program Plan Progress:  
99.67%

Installation Progress

(Blank)!  
Master Program Plan Progress:  
97.00%

Archi Progress

38.94%!  
Master Program Plan Progress:  
1000.00%

Facade Progress

94%!  
Master Program Plan Progress:  
100.00%

Demolition Progress

(Blank)!  
Master Program Plan Progress:  
100.00%

Filter

Year

2024

▼

Year Month

2024-Nov

▼

All Block

Block

All

Weekly Actual  
Productivity

(Blank)

Weekly Plan  
Productivity

(Blank)

Actual Quantity

156

Plan Quantity

212

Total Quantity

212


Actual %

73.58%

Plan %

100.00%

Block	Target Start	Actual Start	Target Finish	Actual Finish Date	Actual	Planned to Date	Total	Planned Progress %	Actual Progress %	Planned vs Actual	Remarks
3	24/07/2023	24/07/2023	07/08/2023	28/08/2023	62	62	62	100.00%	100.00%	0	
5	24/07/2023	24/07/2023	20/11/2023		60	86	86	100.00%	69.77%	-26	
7	24/07/2023	24/07/2023	26/12/2023		34	64	64	100.00%	53.13%	-30	

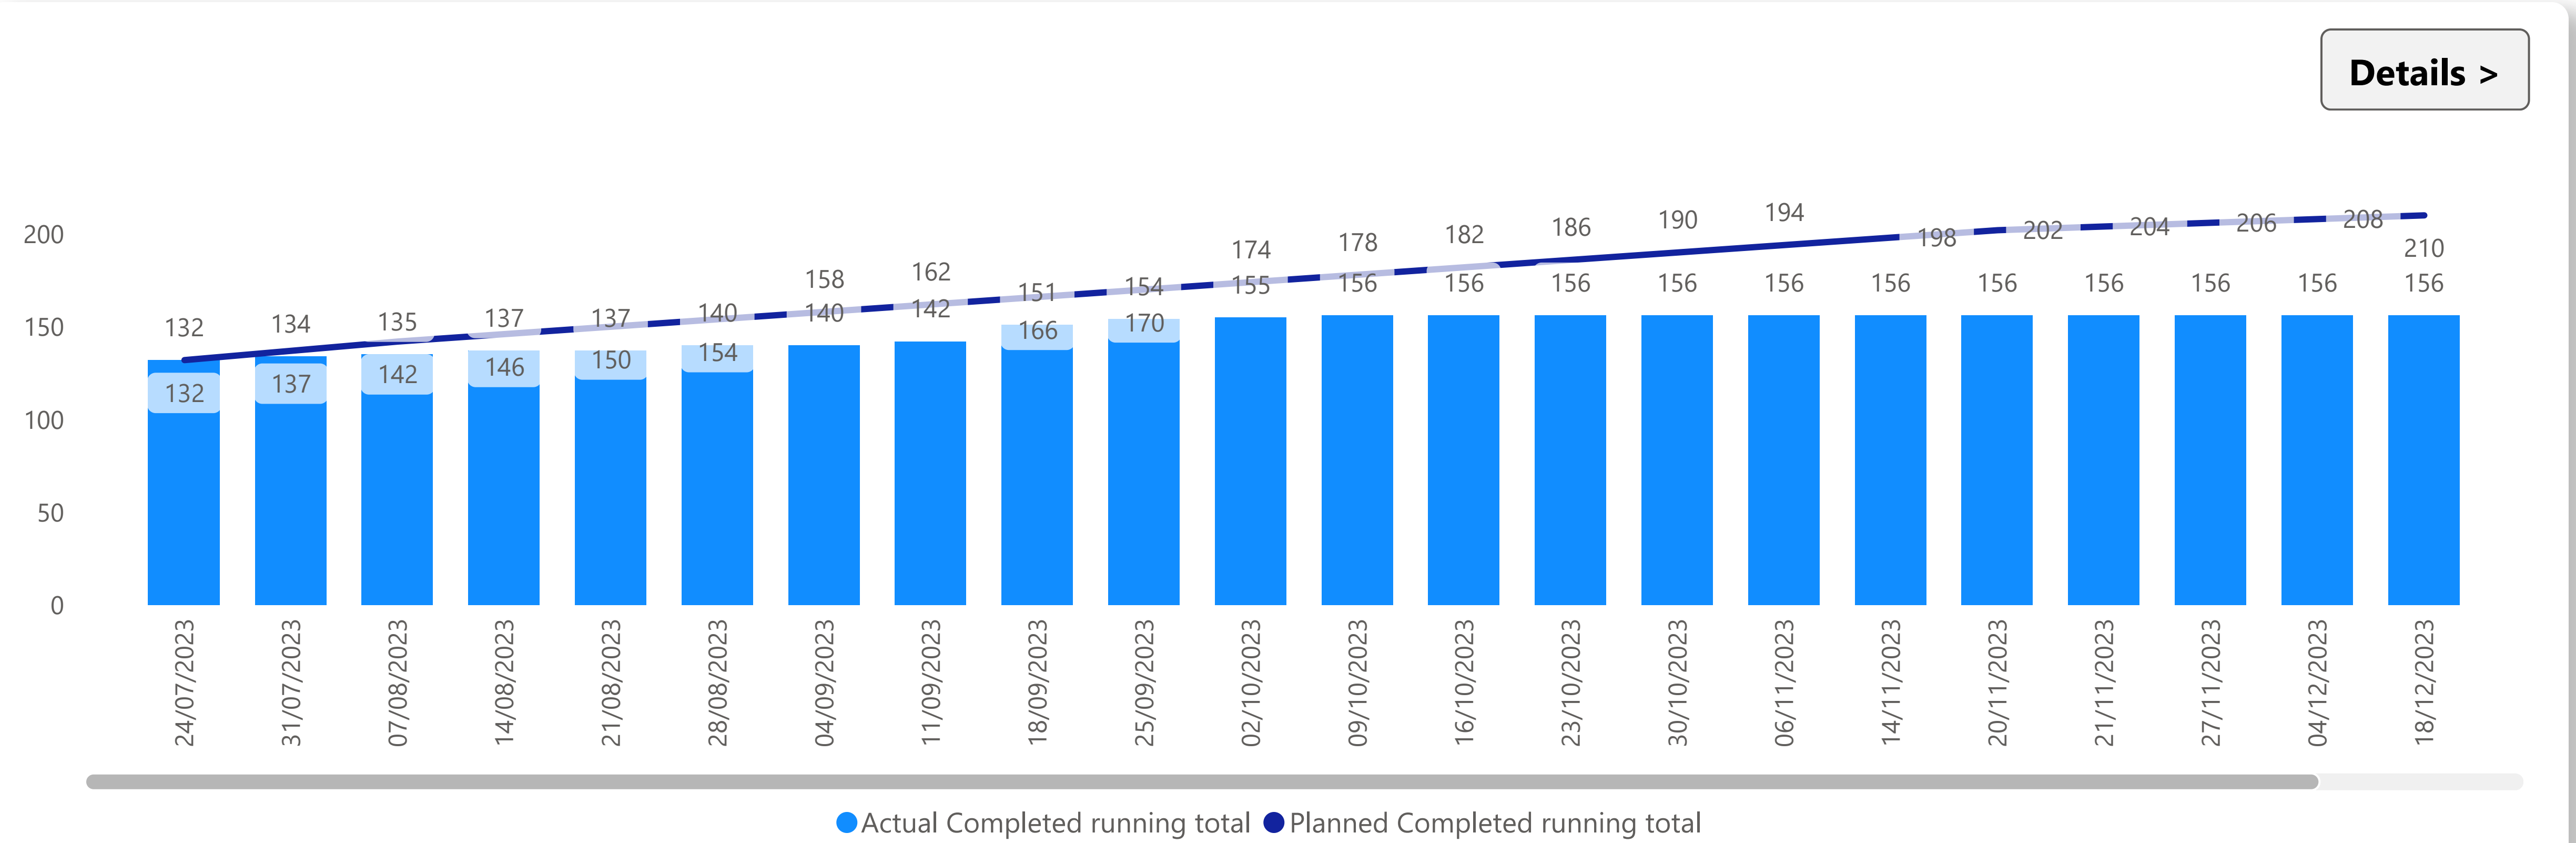

Piling Details

Filter

Year

2024

▼

Year Month

2024-Nov

▼

All Block


Block

All

▼

Weekly Actual Productivity	Weekly Plan Productivity	Actual Quantity	Plan Quantity	Total Quantity	Actual %	Plan %
(Blank)	(Blank)	156	212	212	73.58%	100.00%

Block	Target Start	Actual Start	Target Finish	Actual Finish Date	Actual	Planned to Date	Total	Planned Progress %	Actual Progress %	Planned vs Actual	Remarks
3	24/07/2023	24/07/2023	07/08/2023	28/08/2023	62	62	62	100.00%	100.00%	0	
5	24/07/2023	24/07/2023	20/11/2023		60	86	86	100.00%	69.77%	-26	
7	24/07/2023	24/07/2023	26/12/2023		34	64	64	100.00%	53.13%	-30	

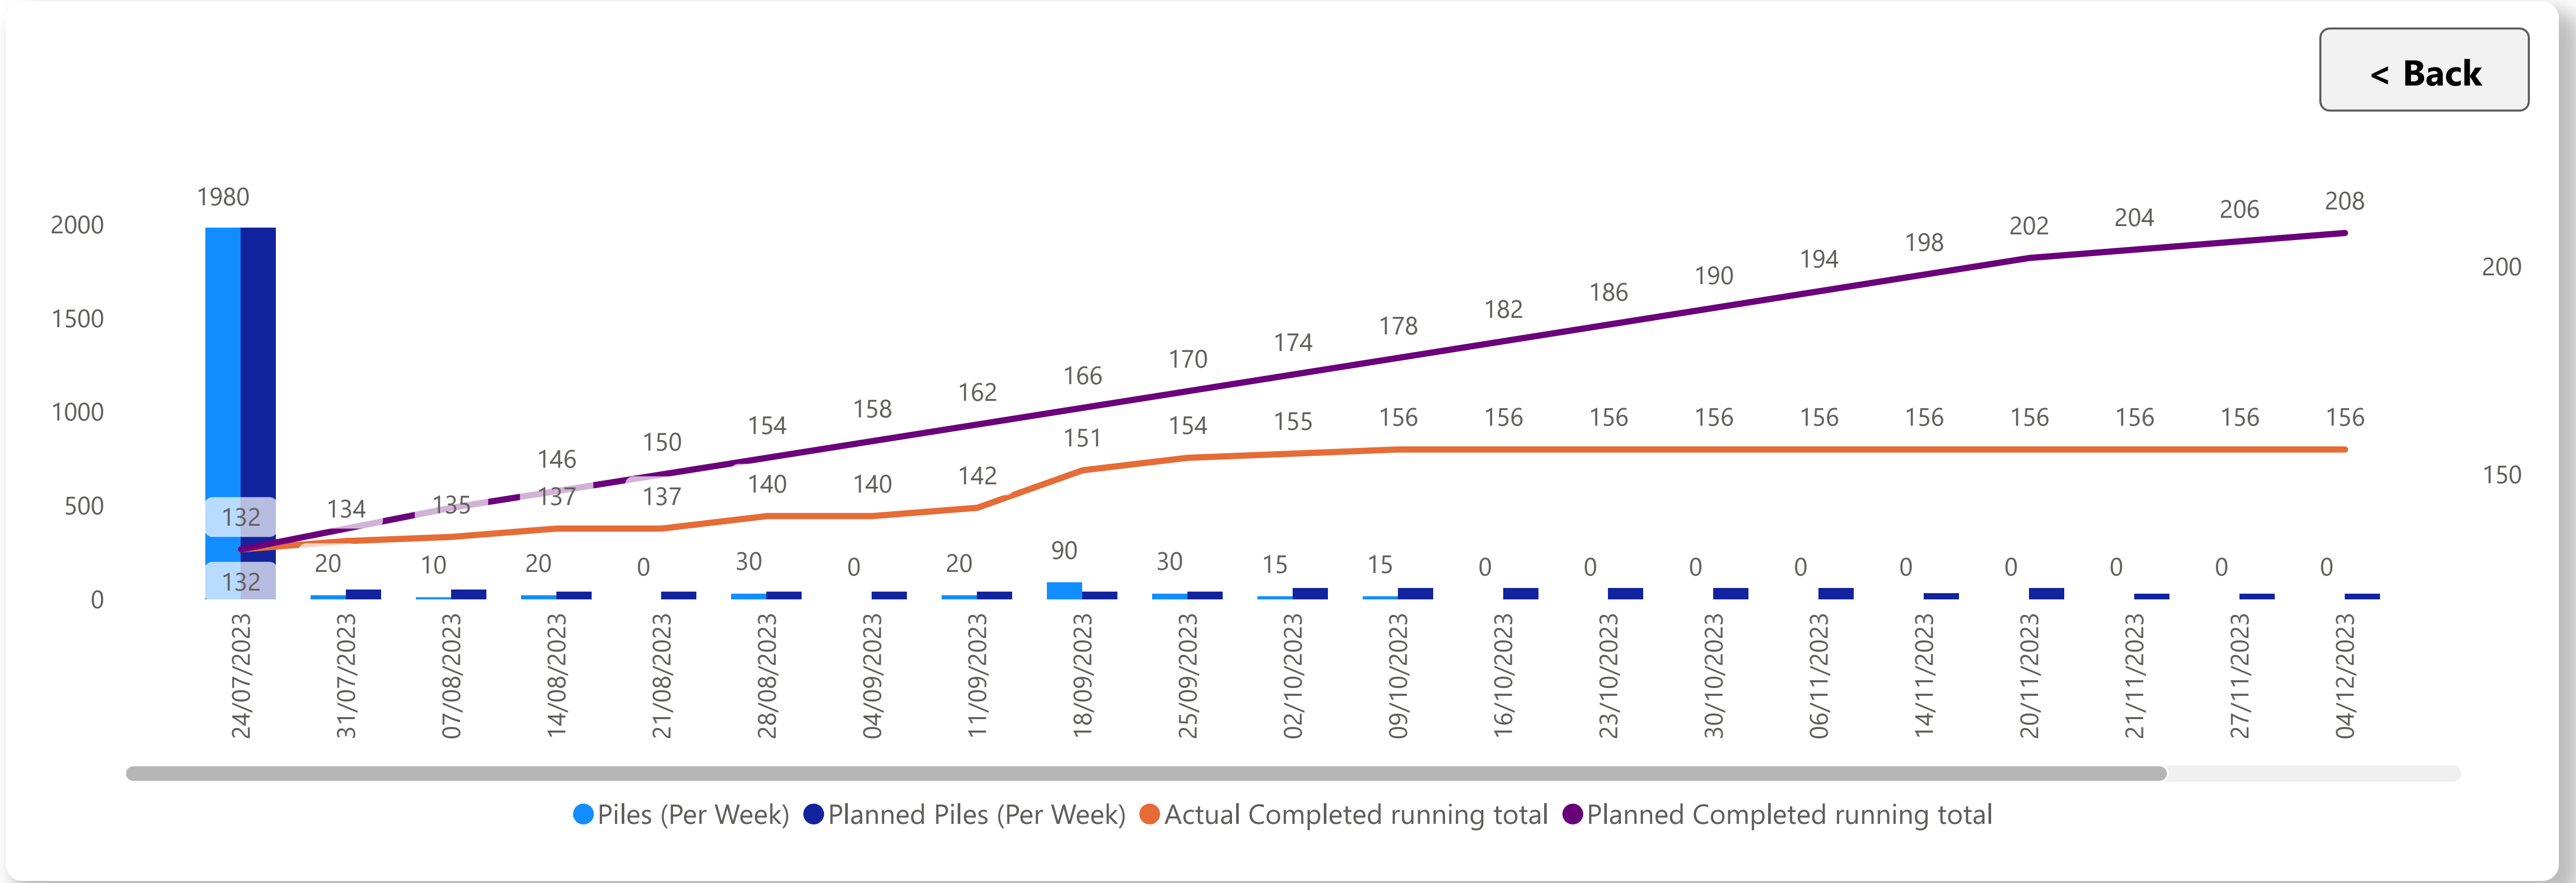

Filter

Year

2024

▼

Year Month

2024-Nov

▼

Casting Progress

15.61%!

MP Plan Progress:  
100.00%

Delivery Progress

5.14%!

MP Plan Progress:  
99.67%

Fit Out Progress

1.54%!

MP Plan Progress:  
99.67%

Installation Progress

(Blank)!

MP Plan Progress:  
97.00%

PPVC Planned % (MP) and PPVC Actual % by Activity Level 3

Details >

● PPVC Planned % (MP) ● PPVC Actual %



Activity Level 3	Block	MP Start Date	MP Finish Date	Estimated Finish Date	MP Plan %	Actual %
Installation	3	30/06/2023	17/09/2024		100.00%	
Delivery	5	15/06/2023	03/10/2024		100.00%	
Fit Out	5	15/06/2023	03/10/2024		100.00%	
Installation	5	21/07/2023	08/10/2024		100.00%	
Casting	7	15/08/2023	01/11/2024		100.00%	
Delivery	7	15/09/2023	02/12/2024		99.00%	
Fit Out	7	15/09/2023	02/12/2024		99.00%	
Installation	7	20/10/2023	07/01/2025		91.00%	
Fit Out	3	28/05/2023	15/09/2024	15/12/2024	100.00%	4.82%
Casting	5	15/05/2023	03/10/2024	03/10/2025	100.00%	10.07%

PPVC Details

Casting Progress (All Block)

PPVC Actual % by Block

3

26.69%

5

18.97%

Total Modules

2684

Completed

419

Balance Module

2265

PPVC Actual %

15.61%

Module	1		2		3		4		5		6		7	8	9
Level	C4(M)	D1	C4(M)	D1	C4(M)	D1	C4(M)	D1	C4(M)	D1	C3	D1	C3	C3	C3
25															
24															
23															
22															
21															
20															
19															
18															
17															
16															
15															
14	Garden	Garden	Garden	Garden	Garden	Garden	Garden	Garden	Garden	Garden	Garden	Garden	Garden	Garden	Gai
13															

Average Production Rate  
(#Modules/day)

3.15


Estimated Days to Completion

718.96

Estimated Completion Date

14/11/2026

Count of Actual Completion Date by Year Month

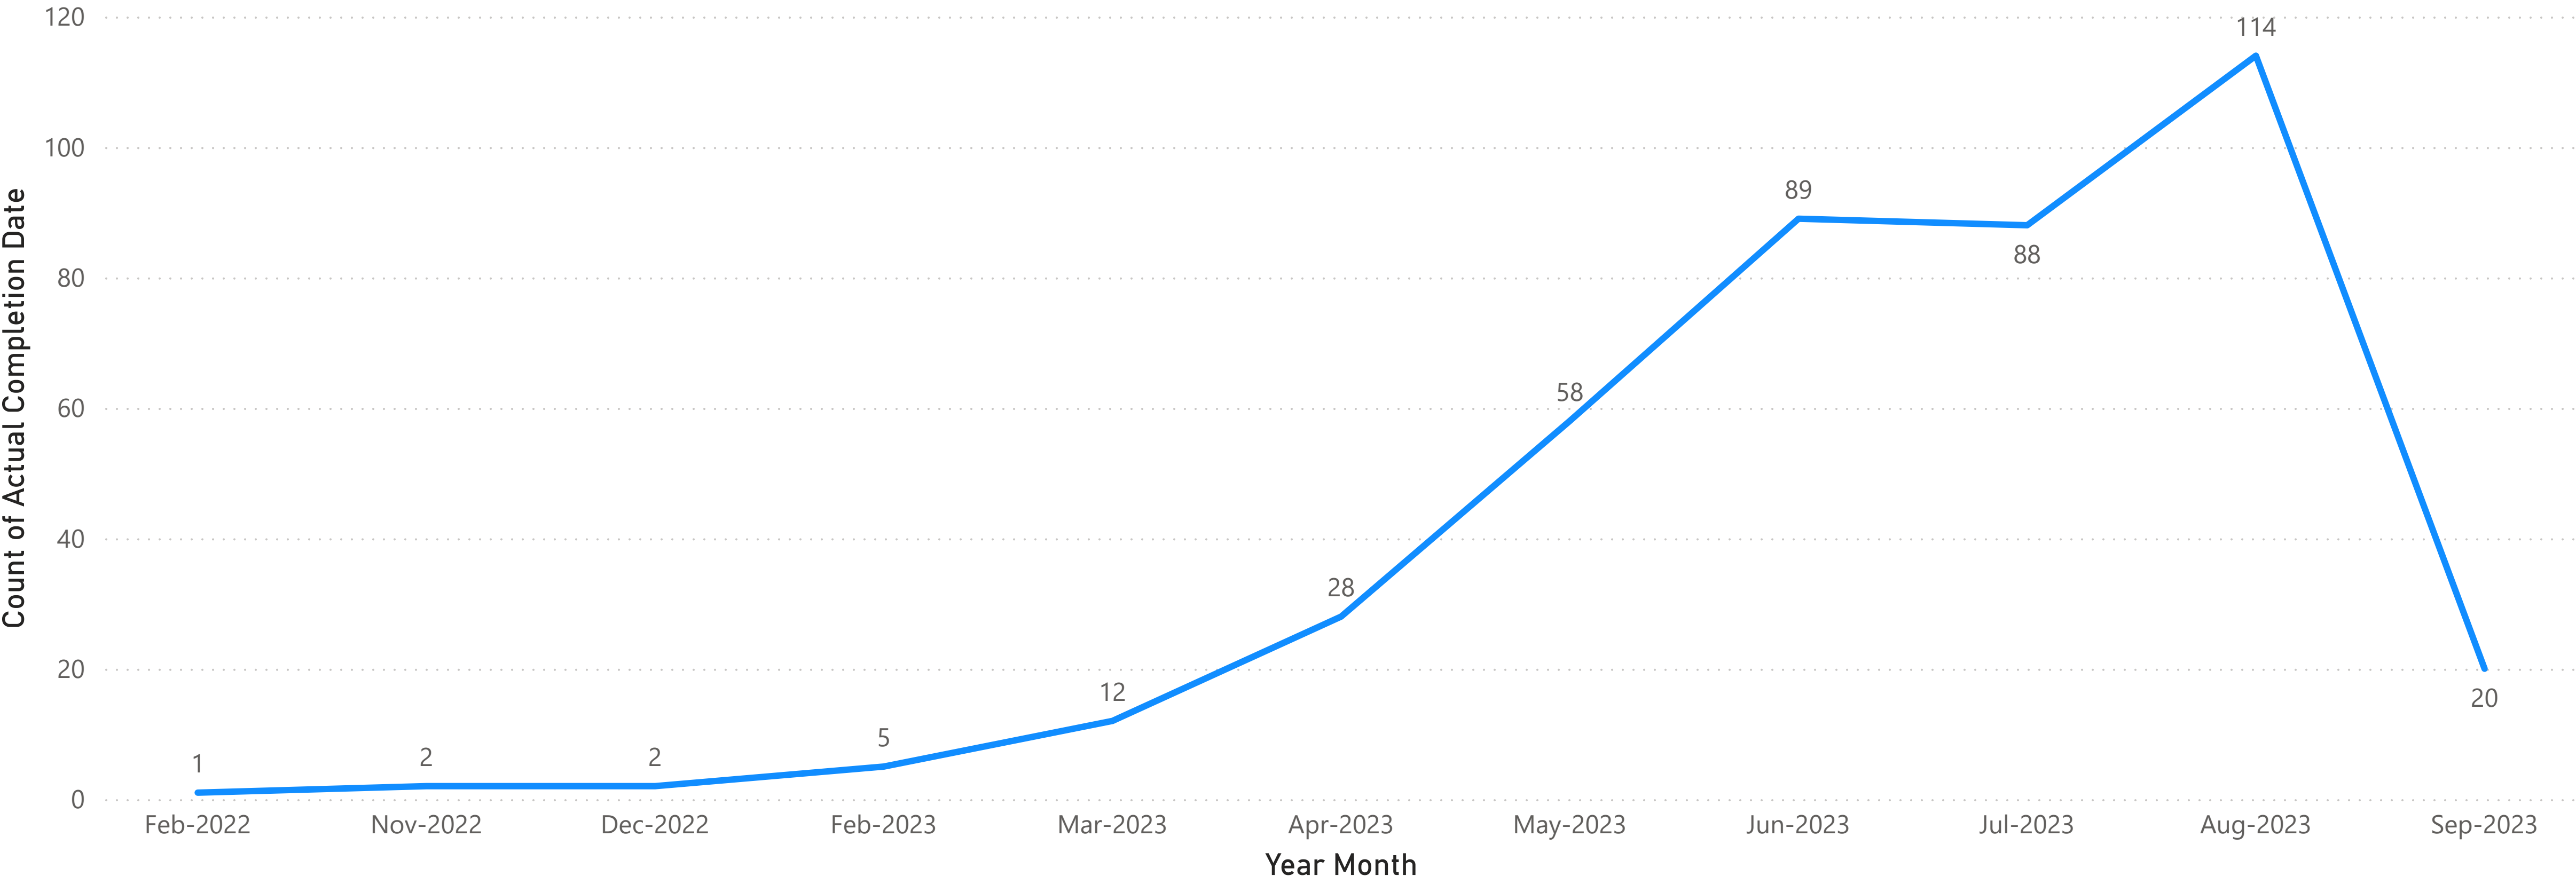

Filter

Year

2024

▼

Year Month

2024-Nov

▼


Details >

38.94%!

MP Plan Progress: 1000.00%

Block	MP Start Date	MP Finish Date	MP Plan %	Archi Actual %
	02/09/2022	14/06/2023	1000.00%	38.94%

Workdone (%) by Block

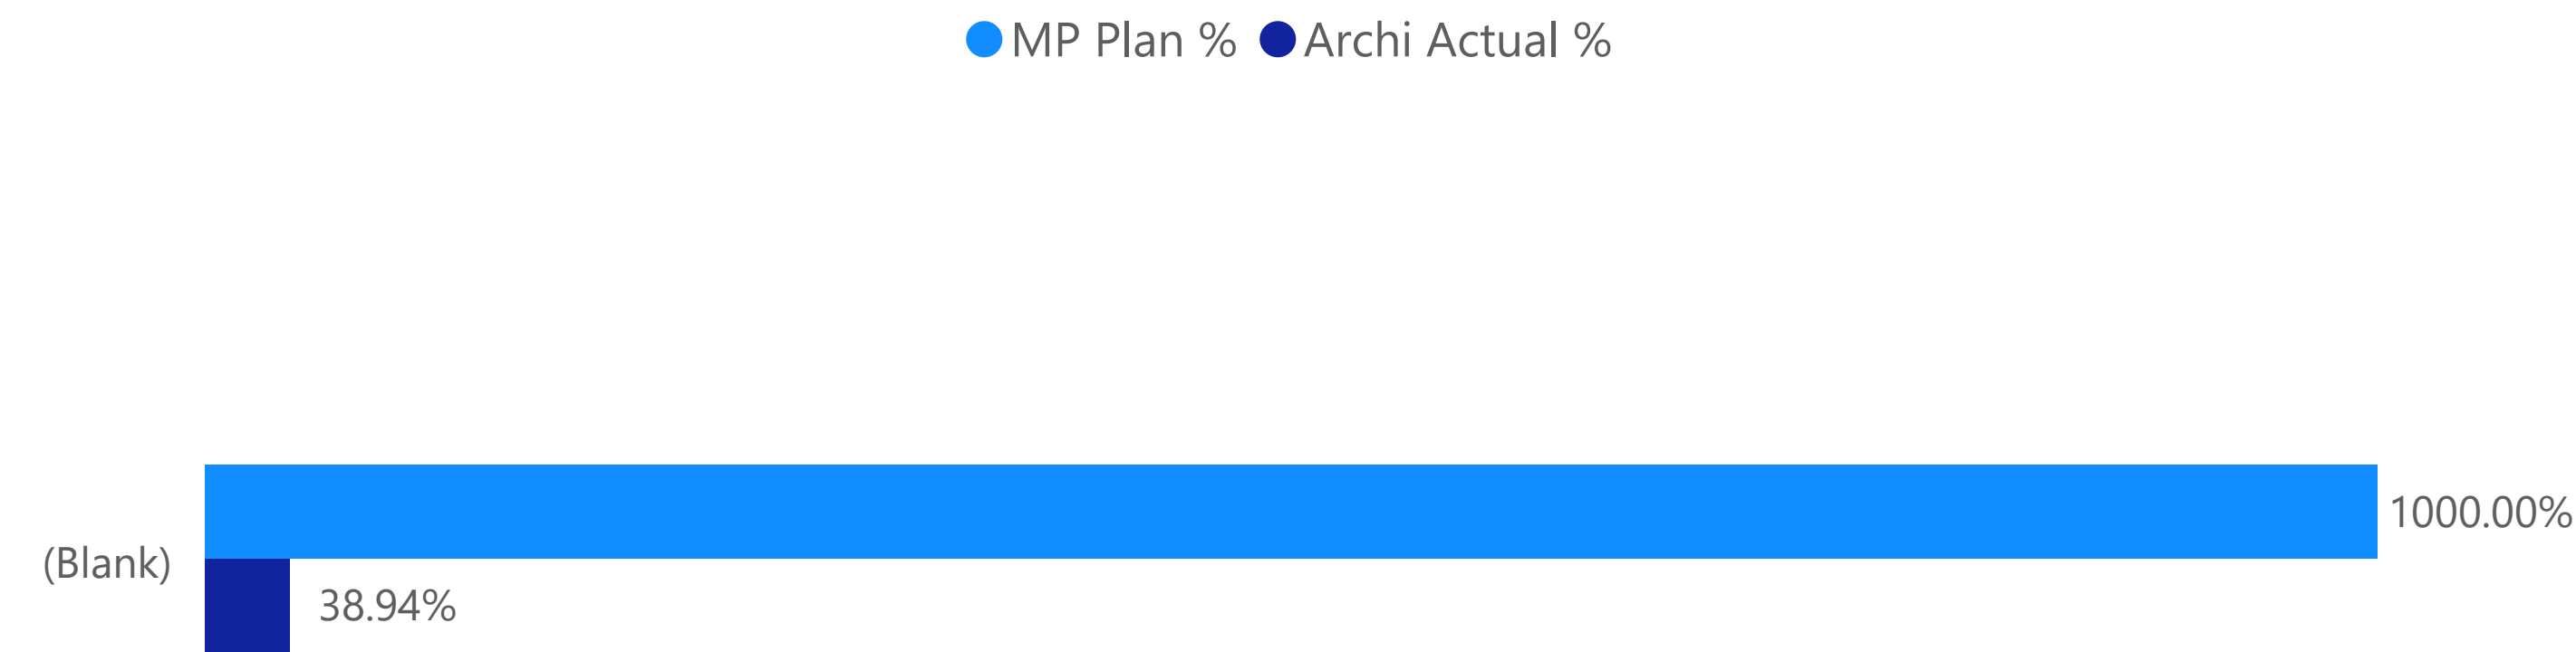



# Architectural Details

Filter

Year

2024

▼

Year Month

2024-Nov

▼

< Back

Architectural Actual %

33.01%

Architectural Trades

- ▼ ☐ BALCONY WORKS
- ▼ ☐ DRY AREA WORKS
- ▼ ☐ GENERAL WORKS
- ▼ ☒ WET AREA WORKS

Architectural Trades									
Block		BATHROOM / KITCHEN ACCESSORIES & FITTING	CEILING BOARD INSTALLATION	CEILING FRAME INSTALLATION	KITCHEN CABINET CARCASS	KITCHEN CABINET DOOR & DRAWERS	KITCHEN HOOD & HOB	KITCHEN SINK	KITCHEN TAP
▲									
⊕	2	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	
⊕	6	0.00%	42.22%	42.22%	0.00%	0.00%	0.00%	0.00%	
⊕	8	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	
⊕	10	16.36%	72.36%	73.73%	37.73%	11.82%	5.00%	18.64%	
⊕	12	44.44%	88.89%	88.89%	47.22%	47.22%	47.22%	47.22%	
⊕	14	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	
⊕	16	0.00%	47.78%	53.33%	0.00%	0.00%	0.00%	0.00%	
⊕	18	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	
⊕	20	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	
⊕	22	67.86%	100.00%	100.00%	89.29%	64.29%	64.29%	89.29%	

Filter

Year

2024

Year Month

2024-Nov

Facade Trades

All

Elevation

All

Block

All

Completed  
(Levels)

41

Pending  
(Levels)

3

Planned Completion Date

12/07/2023

Completed


4125

Estimated Completion Date  
(based on Actual Progress)

10/08/2023

Total to be Installed

4400

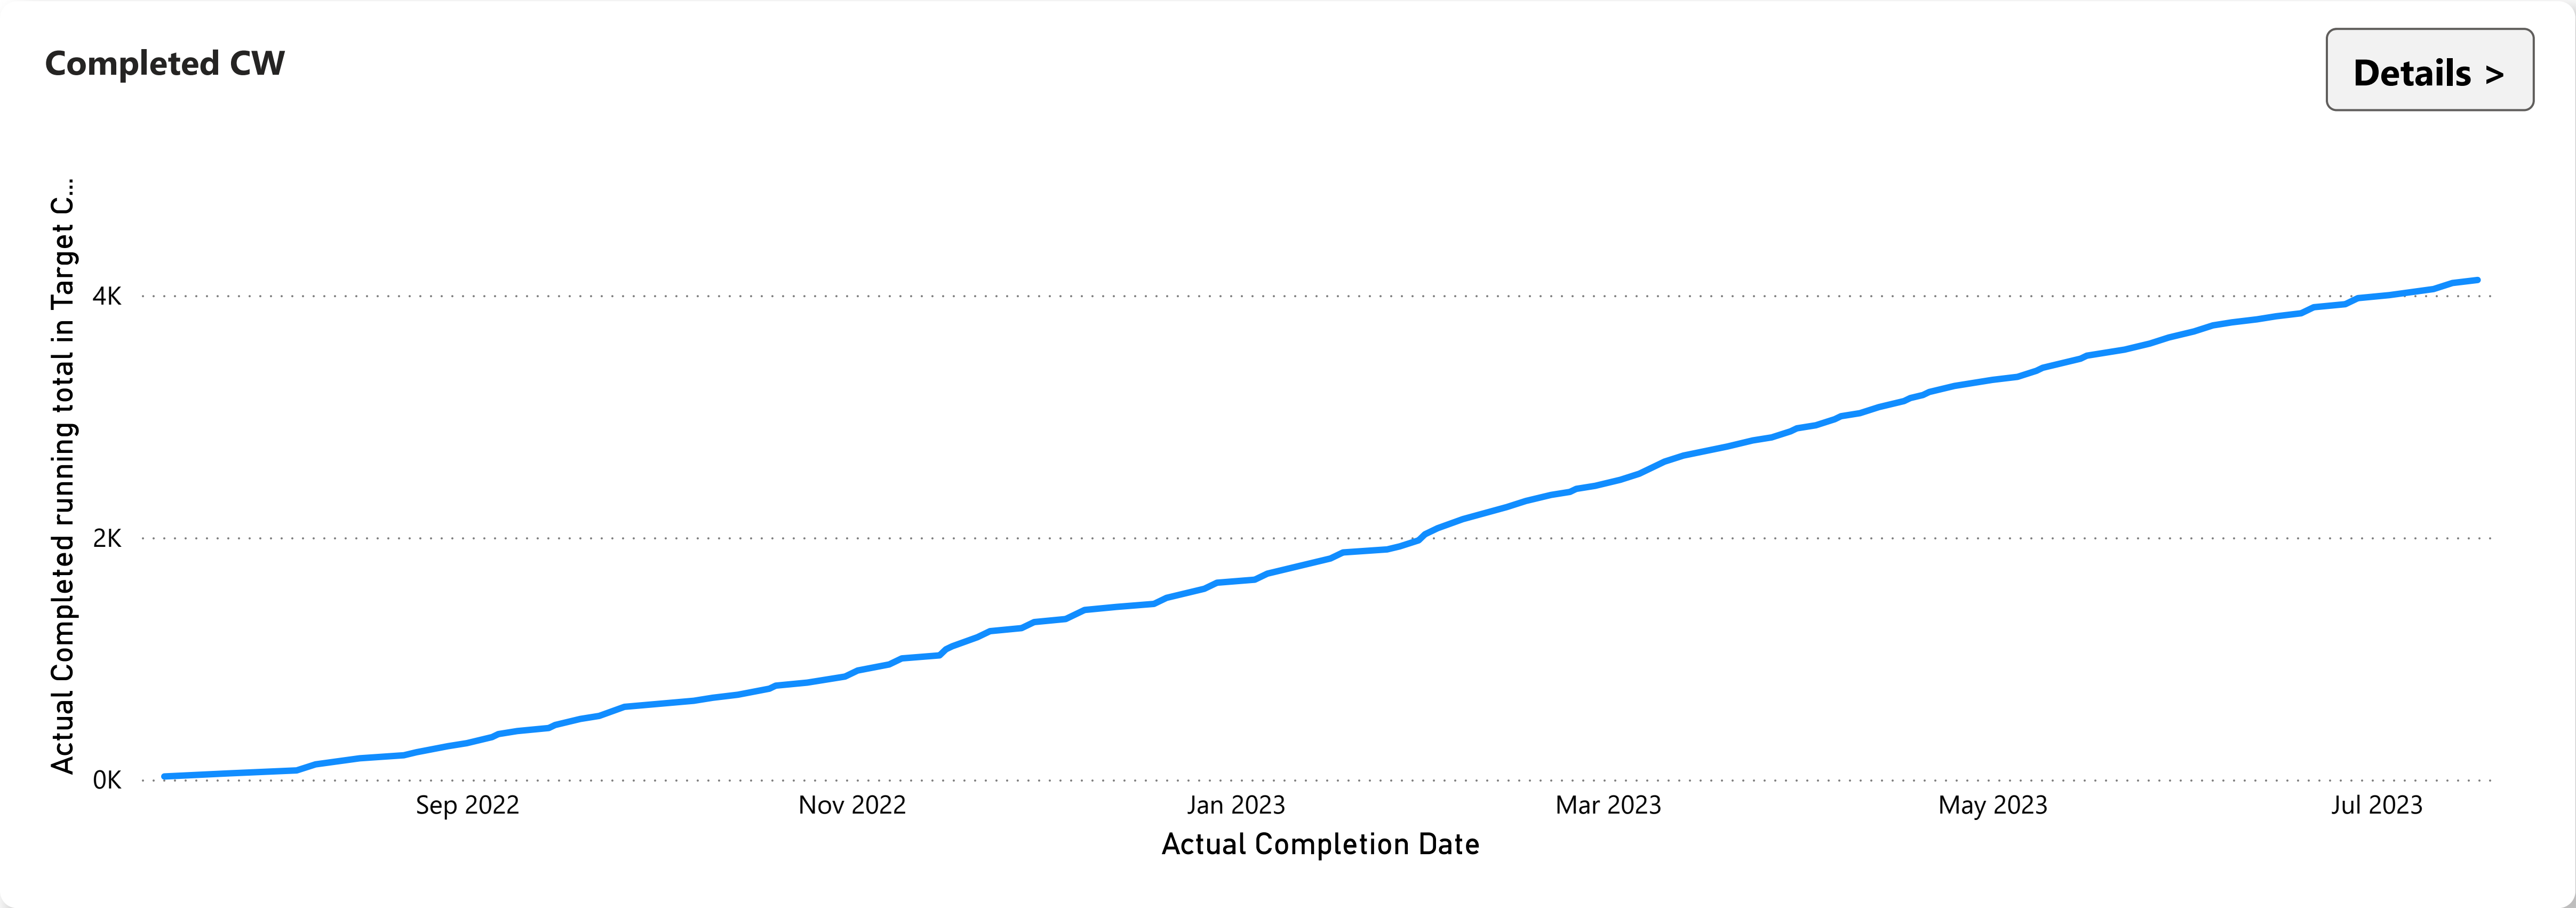



< Back

Filter

Year

Year Month

2024

2024-Nov

Facade Details

Facade Trades

Elevation

All

All

Completed  
(Levels)

41

Pending  
(Levels)

3

Completed

4125

Overall % of Completion

94%

Catch Up Rate/day

-55.00

Planned Completion Date

12/07/2023

Estimated Completion Date  
(based on Actual Progress)

10/08/2023

Level	Target Completion Date	Actual Completion Date	Actual Completed	Days Delay	Expected Rate/day	Actual Rate/day	Catch Up Rate/day	% of Completion
48	12/07/2023		0	-503	4.25			0%
47	05/07/2023		0	-510	4.25			0%
46	21/06/2023	17/07/2023	100	-26	4.25	11.24	-55.00	100%
45	13/06/2023	10/07/2023	100	-27	4.25	11.25	175.00	100%
44	05/06/2023	27/06/2023	100	-22	4.25	11.38	30.00	100%
43	28/05/2023	15/06/2023	100	-18	4.25	11.42	21.30	100%
42	20/05/2023	05/06/2023	100	-16	4.25	11.54	17.57	100%
41	12/05/2023	29/05/2023	100	-17	4.25	11.48	17.05	100%
40	04/05/2023	22/05/2023	100	-18	4.25	11.41	16.67	100%
39	26/04/2023	15/05/2023	100	-19	4.25	11.43	15.95	100%
38	19/04/2023	05/05/2023	100	-16	4.25	11.31	15.81	100%
37	12/04/2023	25/04/2023	100	-13	4.25	11.44	14.74	100%

# Demolition

Filter

Year

2024

▼

Year Month

2024-Nov

▼

Activity Level 3

All

▼

Completed (Levels)

/

Planned Avg. Cycle Time  
(days/level)



(Blank)

Avg. Cycle Time (days/ level)



(Blank)

MP Completion Date

20/07/2024

Planned Completion Date

(Blank)

Estimated Completion Date  
(based on Avg, Cycle Time)



(Blank)

Planned vs Actual Progress of Demolition

Details >

Actual Levels Completed

**< Back**

## Demolition Details

Filter

2024

2024-Nov

Completed (Levels)

/

/

**Planned Avg. Cycle Time**  
**(days/level)**

**(Blank)**



**Avg. Cycle Time (days/ level)**

**(Blank)**



(Blank)

MP Completion Date

20/07/2024

20/07/2024

Planned Completion Date

(Blank)

(Blank)

**Estimated Completion Date**  
(based on Avg, Cycle Time)

**(Blank)**



(Blank)

**Actual Completion**

Level	Actual Start Date	Actual Completion Date	Cycle Time (Actual)	Cycle Time (Planned)
-------	-------------------	------------------------	---------------------	----------------------

### Planned Completion

Level	Target Start	Target Completion
-------	--------------	-------------------
